


F-102 MILESTONE CHART

15 JANUARY 1954
REVISION- 1 APRIL 1955

FISCAL YEAR
CALENDAR YEAR

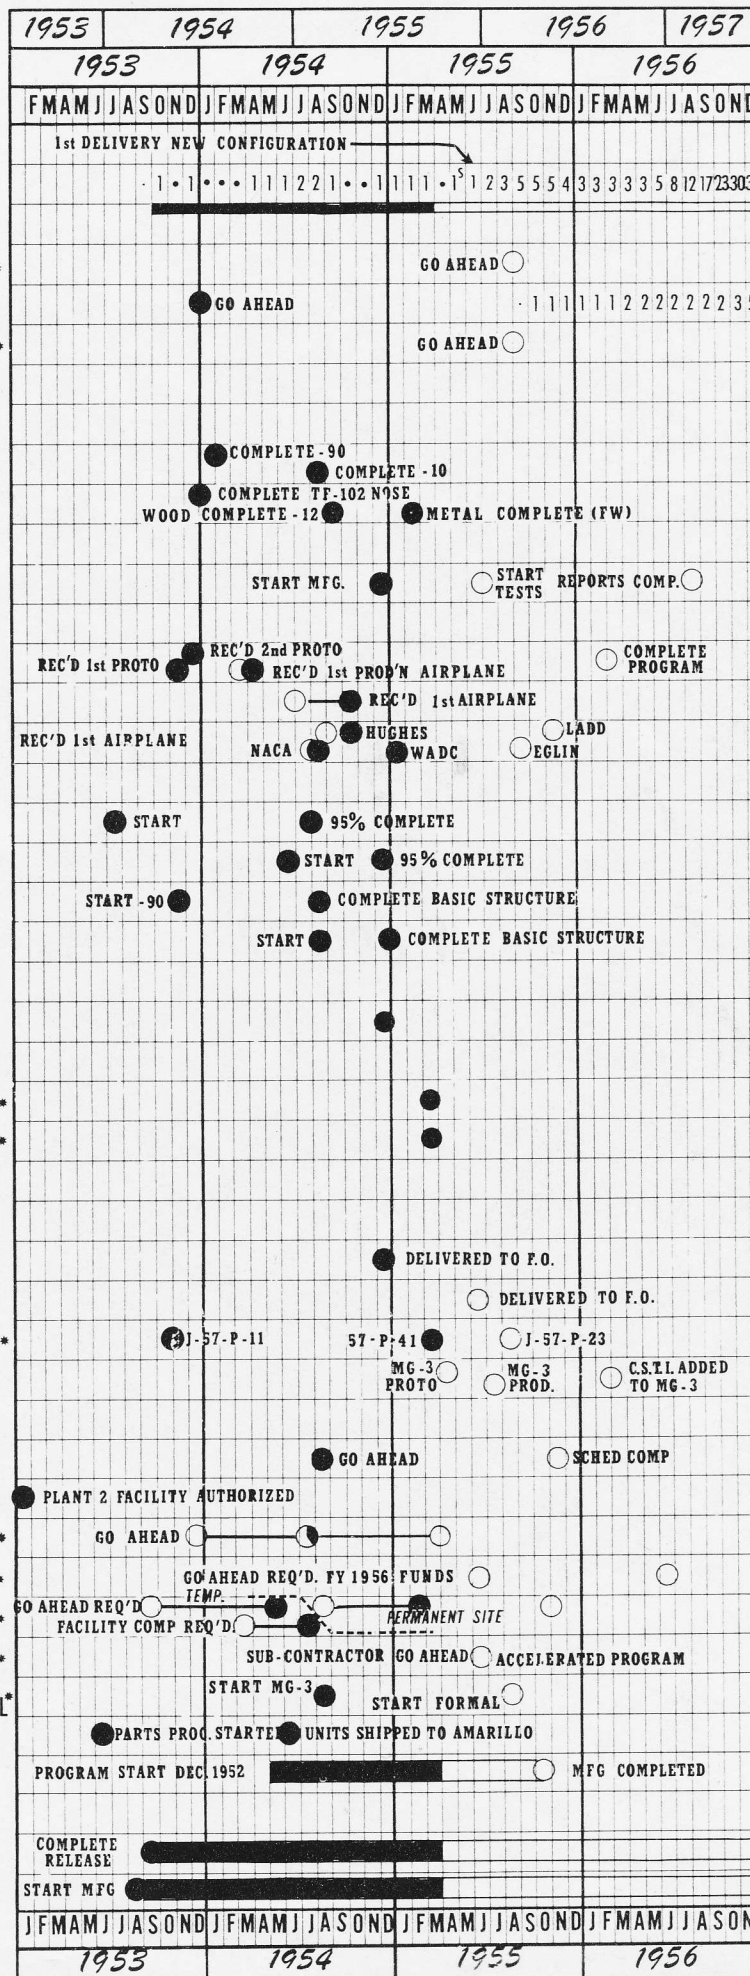

LEGEND

SCHEDULE ○
ACTUAL ●
SCHEDULE SLIPPAGE ○—●

MAY 1955 DELIVERY STATIC A/P

NEGOTIATED PROCUREMENT AVAILABLE IN FISCAL BUDGET 1954

PLANNED FY 1956 CARRY-ON 562 A/P

SCHEDULE REVISION PROPOSED AMC

PLANNED FY 1956 CARRY-ON 150 A/P

COMPLETED DEC. 1952
REVISIONS CONTINUING

REVISED MOCK-UP

APRIL 6, 1954 (1st PROD'N)

-90: IDEAL BODY
-10: LIGHT WEIGHT

TO SUPPORT 8-10 PROGRAM

NO.1 DELIVERED 2 WEEKS EARLY
NO.2 FLOWN JAN. 11, 1954

START MFG. OCT. 1953

START MFG. SEPT. 1954

MX 1179 AUG. 1957

DOUGLAS AIRCRAFT CORP.
PRIME CONTRACTOR

PLANT 2 LEASED JAN. 1951

SA 5 - \$771,290 SUP III REVISED
SA 6 - \$174,190 7 JAN 1955

FACILITIES INSTALL. START SEPT. 1952
1956: \$10,888,728 1957: \$12,098,314

SUBMIT REVISED MASTER LAYOUTS
TO USAF 15 APRIL 1955

MAKE or BUY ACTION COMPLETED

BLDG 43 SITE SELECTED

GO AHEAD DEC. 1952

GO AHEAD APR. 1952
FIRST RELEASE SEPT. 1952

ENGINEERING START APR. 1953

* REVISION

II
